

# IEEE P802.3ba 40Gb/s and 100Gb/s Ethernet Task Force

## Chief Editor's Closing Report

---


Ilango Ganga, Intel  
Editor-in-Chief, IEEE P802.3ba Task Force

May 7, 2009

# D2.0 Comments report (revised)

Description	Editor	Clause	TR	T	ER	E	Total
Front matter, MAC, 40G & 100G Intro	Ilango Ganga	99, 00, 01, A, 4, 4A, 31B, 80	29	14	20	27	90
Management	Hugh Barrass	30, 45	22	29	24	45	120
RS/MII and PCS	Mark Gustlin	81, 82	23	15	7	21	66
PMA	Steve Trowbridge	83, 83C	11	3	9	11	34
XLAUI/CAUI	Ryan Latchman	83A, 83B	33	53	17	14	117
Backplane KR4 related	Arthur Marris	69, 69A, 69B, 73, 74, 84	24	15	18	7	64
Copper CR4 & CR10	Chris Di Minico	85	43	53	13	29	138
Optical SR4 & SR10	Piers Dawe	86	30	45	24	17	116
Optical 40G LR4	Jonathan King	87	3	14	6	3	26
Optical 100G LR4 & ER4	Pete Anslow	88	9	8	8	2	27
Total comments			227	249	146	176	798

# D2.0 Comments distribution (revised)

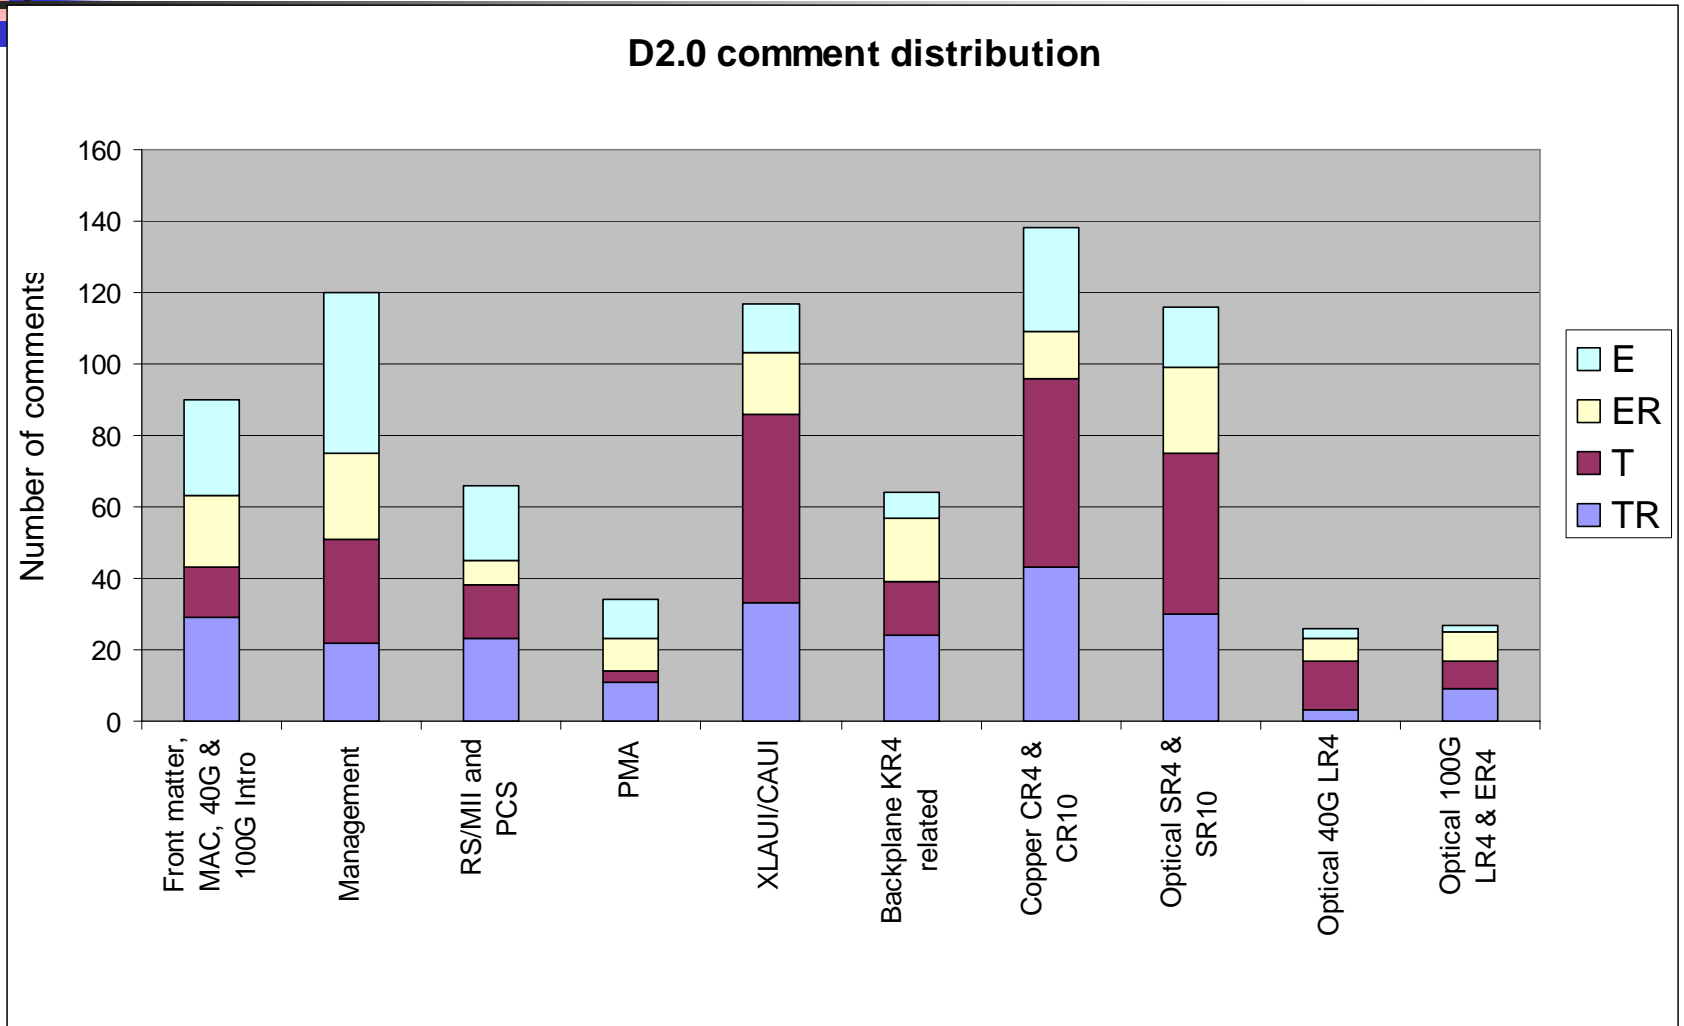




# Progress made in the meeting

---

- Achieved all meeting goals
- Resolve/respond to comments received on D2.0
  - Reviewed all T(249), TR (227) and ERs (146) in the meeting
  - TRs and ERs need signoff from commenters
  - Reviewed 21 out of 176 Es in the meeting, the rest of the Es will be closed as per proposed responses recorded in the database.
- Request to generate D2.1, for WG recirculation, based on D2.0 and recorded comments in the database
- Thanks to the Task Force, Editorial team, volunteers and contributors for your efforts in reviewing and resolving the comments during the meeting

# IEEE P802.3ba Task Force Timeline

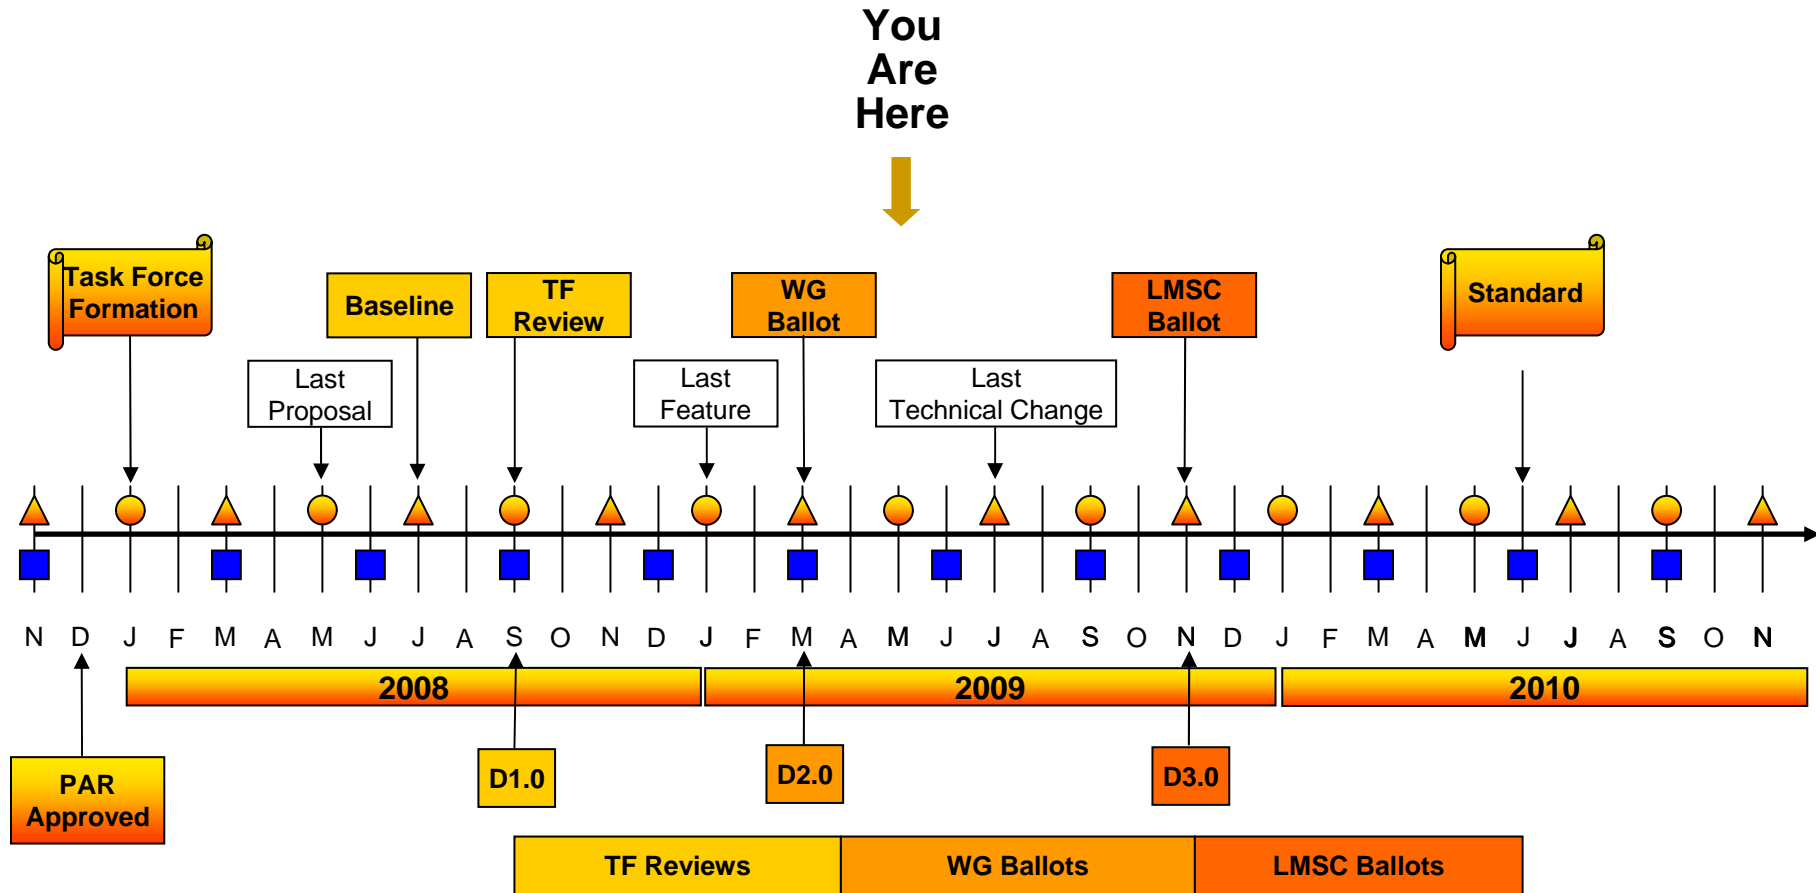

\* Adopted by IEEE P802.3ba TF at March 08 Plenary

Legend	
▲	IEEE 802 Plenary
●	IEEE 802.3 Interim
■	IEEE-SA Standards Board

# Proposed schedule for till Sponsor ballot

Sl.#	Description	Date	Day	# of business days	# of calendar days	Status/Remarks
	Mar Plenary meeting (Mar 9 to Mar 12)	12-Mar	Thu			
	Initial Working Group ballot D2.0 - Opens	12-Mar	Thu			Done
	Initial Working Group ballot D2.0 - Closes	16-Apr	Thu		35	Done
	Proposed response posted	30-Apr	Thu	10		Done
	May interim meeting ends (May 4 to May 7)	7-May	Thu			
	D2.1 Editing starts on following Mon	11-May	Mon			
	First WG ballot recirculation D2.1 - Opens	2-Jun	Tue	16		
	First WG ballot recirculation D2.1 - Closes	27-Jun	Sat		25	25 day circulation (3+ weeks)
	Proposed response posted	9-Jul	Thu	9		reduce time for proposed response
	July Plenary meeting (Jul 13 to Jul 16)	16-Jul	Thu			
	D2.2 Editing starts on following Mon	20-Jul	Mon			
	Second WG ballot recirculation D2.2 - Opens	13-Aug	Thu	18		
	Second WG ballot recirculation D2.2 - Closes	3-Sep	Thu		21	21 day recirc
	Proposed response posted	17-Sep	Thu	10		
	Sep interim meeting (Sep 21 to Sep 24) Estimated	24-Sep	Thu			Dates may move up by 1wk to Sep 14
	D2.3 Editing starts on following Mon	28-Sep	Mon			
	Third WG ballot recirculation D2.3 - Opens	14-Oct	Wed	12		**2wks+2d for draft complete
	Third WG ballot recirculation D2.3 - Closes	29-Oct	Thu		15	15 day recirc
	Proposed response posted	12-Nov	Thu	10		Requirement to req Sponsor ballot: No new negative votes and No substantive (normative) changes
	Nov Plenary meeting (Nov 16 to Nov 19)	19-Nov	Thu			D3.0 ready at closing plenary
	D3.0 Document ready	20-Nov	Fri	1		EC approval on Friday 11/20
	Initial Sponsor ballot D3.0 - Opens	1-Dec	Tue	7		Requires 5 business days before ballot + 2 days for Thanksgiving
	Initial Sponsor ballot D3.0 - Closes	31-Dec	Thu		30	Min 30 day electronic ballot
	Proposed response posted	14-Jan	Thu	10		Including new year holiday
	Jan interim meeting (Jan 18 to Jan 21) Estimated	21-Jan	Thu			Dates may move + 1 wk



# Summary

---

- Resolved/Responded to comments received on D2.0
  - Please email to Chair, STF Chairs, or Chief Editor if you are satisfied with resolution to your TR/ER comments
- Request to generate D2.1, based on D2.0 and as per recorded comments in the database
- Request to go to 25 day WG recirculation as appropriate
