

IEEE P802.3ba 40Gb/s and 100Gb/s Ethernet Task Force



Chief Editor's Closing Report

Ilango Ganga, Intel
Editor-in-Chief, IEEE P802.3ba Task Force

Sep 24, 2009



WG ballot results (revised*)

D2.2 WG recirculation ballot	
Voters	229
Approve	108
Disapprove	21
Disapprove w/o comment	1
Abstain	14
Returns	144
Response rate	62.88%
Abstention rate	9.72%
Approval rate	83.72%


D2.1 WG recirculation ballot	
Voters	229
Approve	97
Disapprove	30
Disapprove w/o comment	2
Abstain	11
Returns	140
Response rate	61.14%
Abstention rate	7.86%
Approval rate	76.38%

D2.0 Initial WG ballot	
Voters	229
Approve	87
Disapprove	32
Disapprove w/o comment	3
Abstain	10
Returns	132
Response rate	57.64%
Abstention rate	7.58%
Approval rate	73.11%

Ballot met required response rate $\geq 50\%$, abstention rate $< 30\%$, and approval rate $\geq 75\%$

*Revised ballot results at the close of the Sep'09 interim (2 ballot flips at the meeting)

Unsatisfied comments history (revised*)

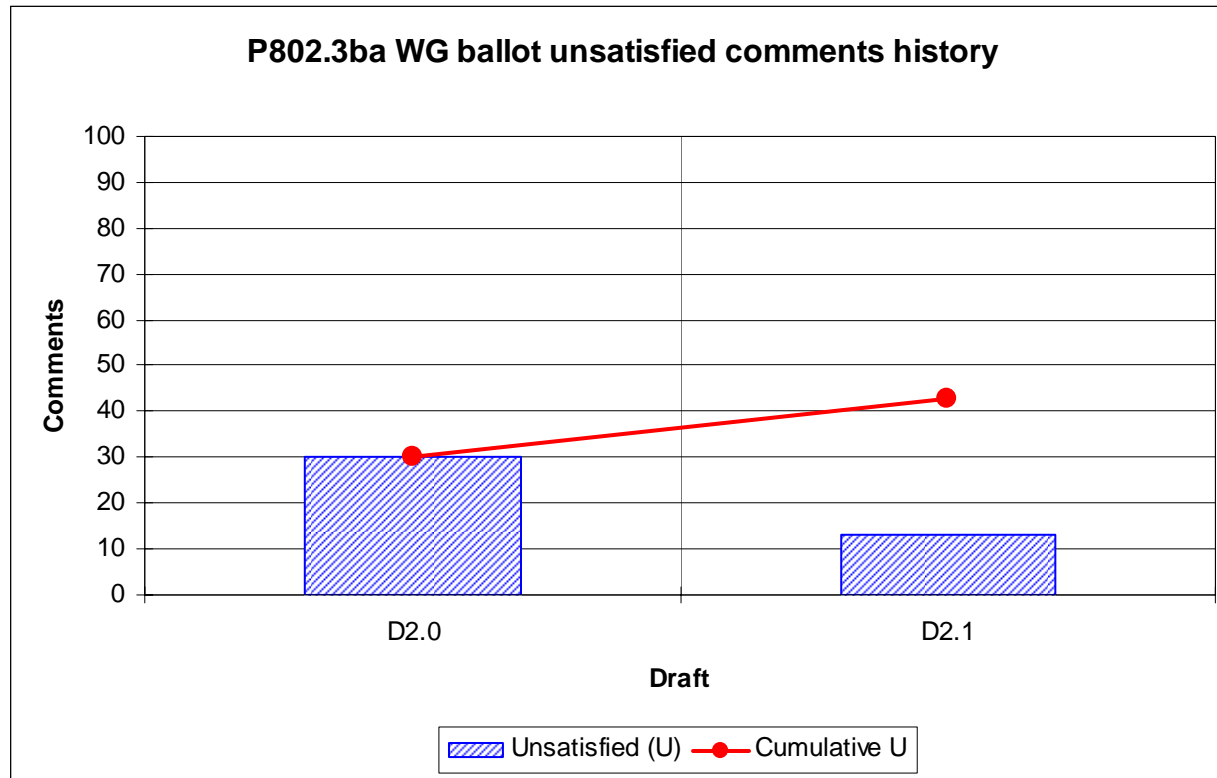


*Revised statistics at the close of the Sep'09 interim (closed 24 negative comments at the meeting)



Progress made in the meeting

- Achieved the meeting goals
- Resolved/responded to all 234 comments received on D2.2
 - Reviewed all T(71), TR (91), E (54) and ERs (18) in the meeting
 - 13 TR/ER comments need signoff from 1 commenter
- Request to generate D2.3, for WG recirculation, based on D2.2 and recorded comments in the database
- Thanks to the Task Force, Editorial team, volunteers and contributors for your efforts in reviewing and resolving the comments during the meeting

IEEE P802.3ba Task Force Timeline

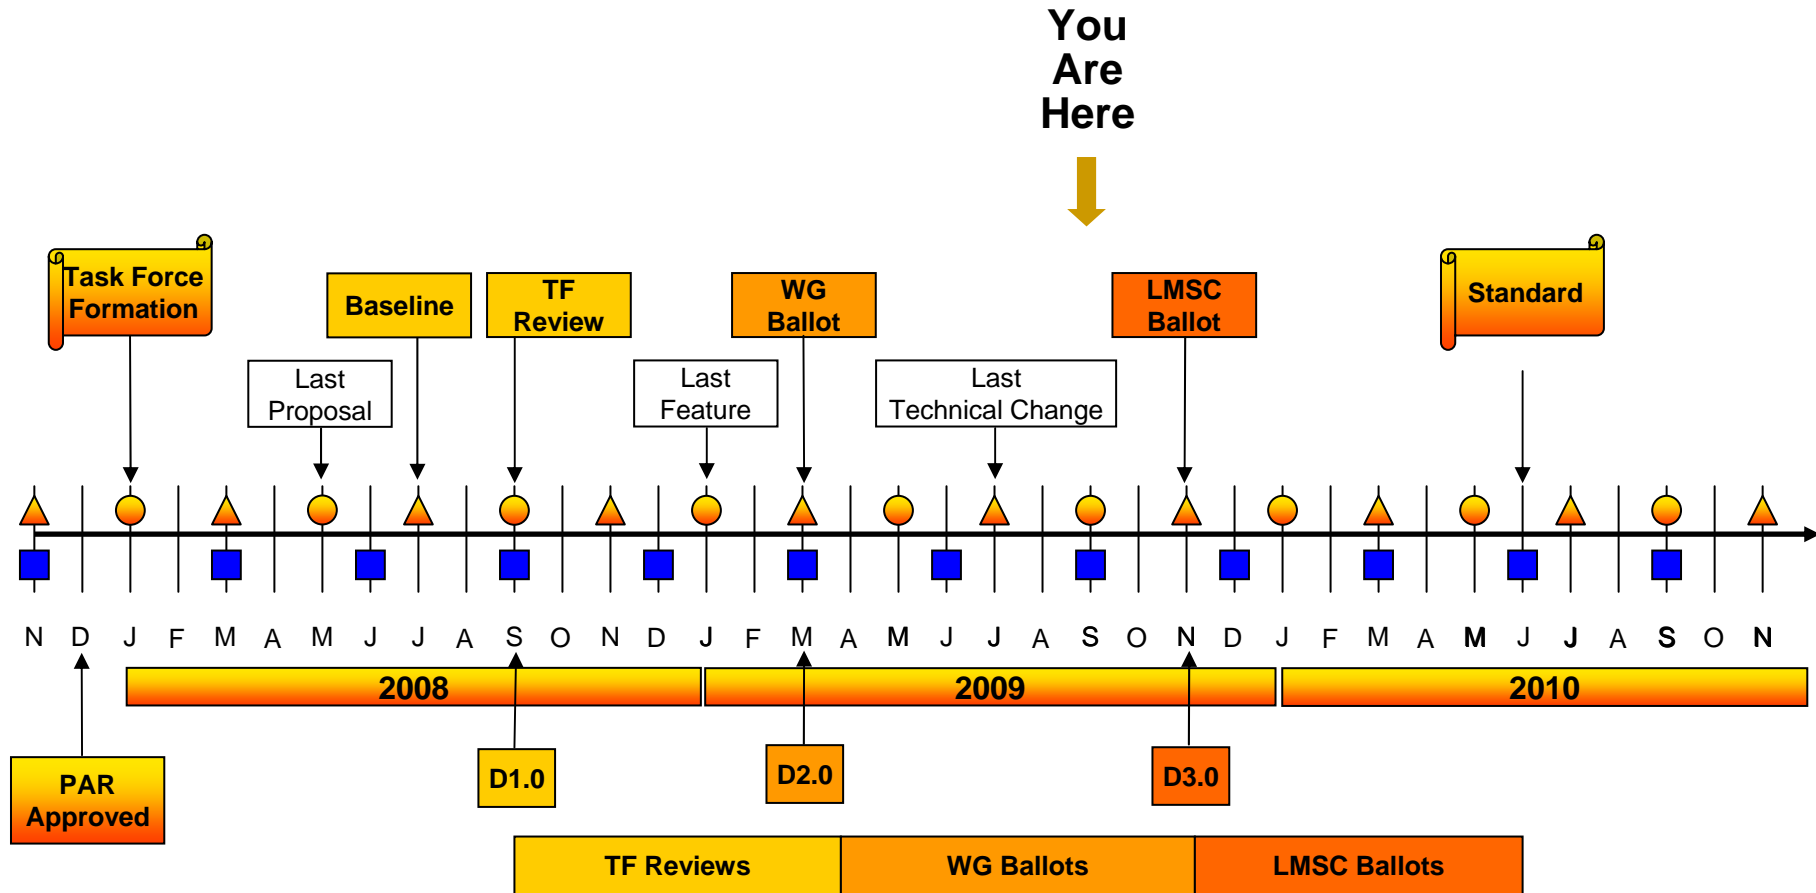

* Adopted by IEEE P802.3ba TF at March 08 Plenary

- Legend**
- ▲ IEEE 802 Plenary
 - IEEE 802.3 Interim
 - IEEE-SA Standards Board

Proposed schedule till Sponsor ballot

Sl.#	Description	Date	Day	# of business days	# of calendar days	Status/Remarks
	Mar Plenary meeting (Mar 9 to Mar 12)	12-Mar	Thu			
	Initial Working Group ballot D2.0 - Opens	12-Mar	Thu			Done
	Initial Working Group ballot D2.0 - Closes	16-Apr	Thu		35	Done
	Proposed response posted	30-Apr	Thu	10		Done
	May interim meeting ends (May 4 to May 7)	7-May	Thu			
	D2.1 Editing starts on following Mon	11-May	Mon			
	First WG ballot recirculation D2.1 - Opens	1-Jun	Mon	15		
	First WG ballot recirculation D2.1 - Closes	26-Jun	Fri		25	25 day circulation
	Proposed response posted	9-Jul	Thu	9		
	July Plenary meeting (Jul 13 to Jul 16)	16-Jul	Thu			
	D2.2 Editing starts on following Mon	20-Jul	Mon			
	Second WG ballot recirculation D2.2 - Opens	19-Aug	Wed	22		
	Second WG ballot recirculation D2.2 - Closes	2-Sep	Wed		15	15 day recirc
	Proposed response posted	17-Sep	Thu	10		
	Sep interim meeting (Sep 21 to Sep 24)	24-Sep	Thu			
	D2.3 Editing starts on following Mon	28-Sep	Mon			
	Third WG ballot recirculation D2.3 - Opens	15-Oct	Thu	13		**2wks+2d for draft complete!!
	Third WG ballot recirculation D2.3 - Closes	29-Oct	Thu		15	15 day recirc
	Proposed response posted	12-Nov	Thu	10		Requirement to req Sponsor ballot. No new unresolved negatives and No substantive (normative) changes
	Nov Plenary meeting (Nov 16 to Nov 19)	19-Nov	Thu			D3.0 ready at closing plenary EC approval on Friday 11/20
	Mandatory Editorial coordination (MEC)	30-Nov	Mon	7		2 days for US Thanksgiving Nov 26-27
	Initial Sponsor ballot D3.0 - Opens	7-Dec	Mon	5		Requires 5 business days before ballot
	Initial Sponsor ballot D3.0 - Closes	5-Jan	Tue		30	Min 30 day electronic ballot
	Proposed response posted	21-Jan	Thu	11		Including new year holiday
	Jan interim meeting (Jan 25 to Jan 29) Estimated	25-Jan	Mon			Estimated dates, subject to change



Summary

- Resolved/Responded to all comments received on D2.2
 - Please email to the Chair, Chief Editor, or STF Chairs, if you are satisfied with resolution to your TR/ER comments
- Request to generate D2.3, based on D2.2 and as per recorded comments in the database
- Request to go to 15 day WG recirculation as appropriate
